

## REINBERG

## Project Summary

Project Type: Exterior Renovation  
 Department: Facilities  
 Status: Completed  
 Unit Number: 25111


**Budget Amount: \$1,300,000**  
 Budget Year: 2010  
 Construction Start Date: June 2010  
 In Service Date: August 2011  
 Anticipated Completion Date: May 2012

The purpose of this project is to remove the temporary modular classrooms which are in poor condition and no longer required.

## Financial Details

Project Phase	Original Budget	Current Estimate:	\$1,482,918
Design:	\$91,875	Expenditure to Date:	\$1,349,224
Construction:	\$1,117,332	Percent Complete:	91%
Environmental:	\$18,167	Funding Source:	CPS Resources
Management:	\$72,627		
<b>Project Total:</b>	<b>\$1,300,000</b>		

## Details

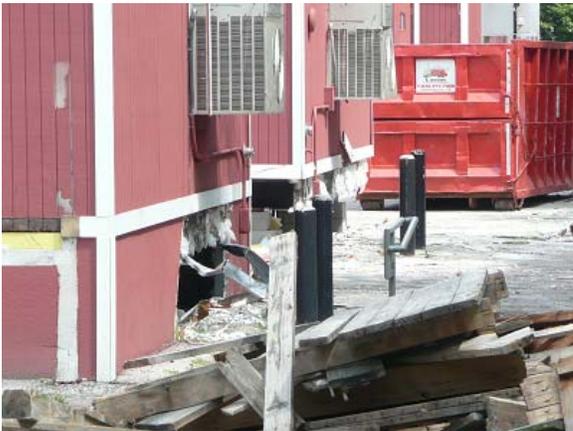

Ideal Program Enrollment: 750  
 2011/2012 Enrollment: 854  
 Space Utilization Index / Status: 14% (efficient)  
 Performance Level: Level 1  
 Building Age: 85 Years  
 Network: O'Hare ES

## Scope

The scope of this project is to remove existing temporary modular classroom units and replace it with an artificial turf field. Additional scope includes replacing exterior wood doors with steel, as well as renovating the lunch room, art room, and music room. The project will address city zoning scope as required.

