

DuSable Campus

Project Summary

Project Type: Exterior Renovation
 Department: Facilities
 Status: Closing
 Unit Number: 46541


Budget Amount: \$26,640,000
 Budget Year: 2011
 Construction Start Date: June 2011
 In Service Date: August 2012
 Anticipated Completion Date: June 2013

The purpose of this project is to replace the roof which is leaking and the windows that have failed. Both systems are beyond their useful life. There is deteriorating masonry which is also contributing to water infiltration.

Financial Details

Project Phase	Original Budget	Current Estimate:	\$25,292,589
Design:	\$1,130,818	Expenditure to Date:	\$21,566,751
Construction:	\$23,592,107	Percent Complete:	85%
Environmental:	\$383,588	Funding Source:	CPS Resources
Management:	\$1,533,487		
Project Total:	\$26,640,000		

Details

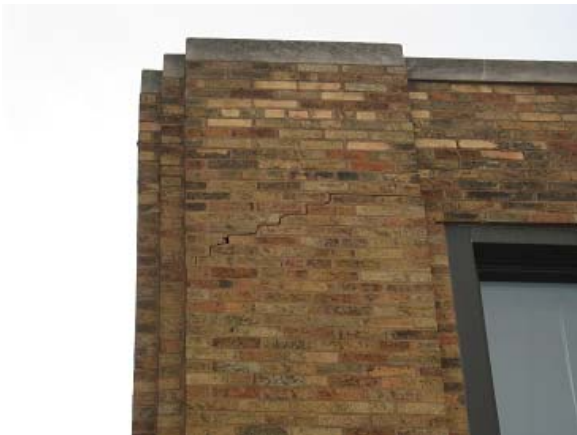

Ideal Program Enrollment:
 2011/2012 Enrollment:
 Space Utilization Index / Status:
 Performance Level:
 Building Age: Years
 Network: South Side HS

Scope

The scope of this project is an extensive exterior renovation. The project includes full roof replacement, full window replacement, repairing and replacing lintels, and extensive masonry repairs. The project will address ADA and city zoning requirements.

