

RYERSON

Project Summary

Project Type: Structural Renovation / Contingency

Department: Facilities

Status: Construction

Unit Number: 25201

Budget Amount: \$20,330

Budget Year: 2012

Construction Start Date: June 2012

In Service Date: June 2013


Anticipated Completion Date: August 2013

The purpose of this project is to address the displaced/cracked masonry at the corner of the parapet and below the cornice. There is also cracked and displaced limestone at main entrance and over other exterior doors.

Financial Details

Project Phase	Original Budget	Current Estimate:	\$10,405
Design:	\$1,815	Expenditure to Date:	\$4,023
Construction:	\$17,124	Percent Complete:	39%
Environmental:	\$278	Funding Source:	CPS Resources
Management:	\$1,113		
Project Total:	\$20,330		

Details

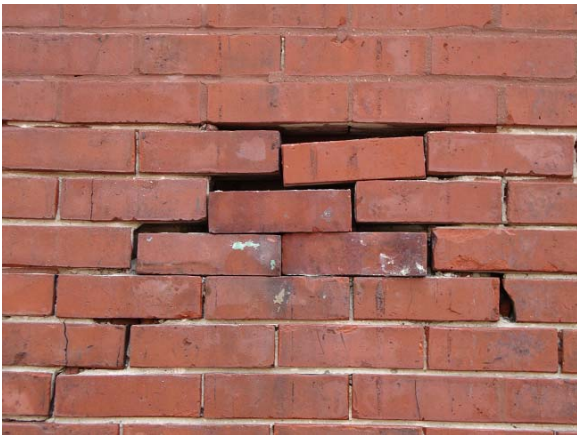

Ideal Program Enrollment: 690

2011/2012 Enrollment: 399

Space Utilization Index / Status: -42% (underutilized)

Performance Level: Level 2

Building Age: 122 Years

Network: Garfield-Humboldt ES

Scope

This project will be funded under FY12, 6.0 Supplemental Facility Renovation and is targeting immediate structural repairs at this facility.

The scope of the required work is:

Locally demolish and rebuild displaced/cracked masonry at corner of parapet and below cornice.

Repair cracked and displaced limestone at entrance.

Locally repair displaced aluminum cornice.

