

GALILEO

Project Summary

Project Type: ADA Improvements
 Department: Facilities
 Status: Completed
 Unit Number: 29141


Budget Amount: \$3,407,255
 Budget Year: 2012
 Construction Start Date: April 2012
 In Service Date: August 2012
 Anticipated Completion Date: December 2012

Galileo is a magnet school. Since it is a special use school, it is required by the Americans Disabilities Act to be accessible.

Financial Details

Project Phase	Original Budget	Current Estimate:	\$3,724,769
Design:	\$220,569	Expenditure to Date:	\$3,143,194
Construction:	\$2,947,199	Percent Complete:	84%
Environmental:	\$47,919	Funding Source:	CPS Resources
Management:	\$191,568		
Project Total:	\$3,407,255		

Details

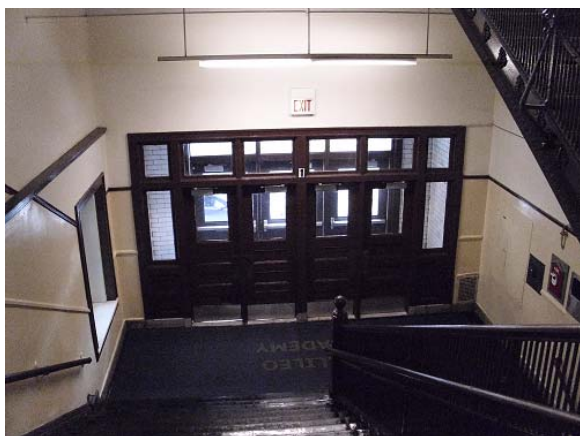

Ideal Program Enrollment: 630
 2011/2012 Enrollment: 603
 Space Utilization Index / Status: -4% (efficient)
 Performance Level: Level 2
 Building Age: 119 Years
 Network: Fulton ES

Scope

New accessible entry with ramp and Aiphone, new lower level ramped access within the building, a fire rated Kiln enclosure in the Art room, new accessible seating in the Auditorium, a Stage Lift in the Auditorium, a new (4) stop 3,000lb exterior elevator connecting all levels, full Toilet room upgrades providing Adult and Child height accessible fixtures, Unisex toilet rooms, Drinking Fountains providing child, adult and reduced bending, accessible student lockers, making existing corridor doors accessible, new interior and exterior building signage, a new Fire Alarm system, accessible parking and Trash Enclosure.
